

DOCKING PROGRESS REPORT – Day 16

Ship Name	GAS NURI ARIZONA
Type of Docking	INTERMEDIATE SURVEY V
Location	Semarang
Main Contractor	PT . YWTS
Date	25 July 2018

PHOTO REPORT



In progress class survey by class KR and transfer of class from ABS to KR. Certificate of Class and Load Line Certificate will be issued on Monday 30/7/2018




Sea water line for cargo re heater han been renewed



Cargo re heater has been serviced




Preparation surface for air pressure test cargo line to check leakage

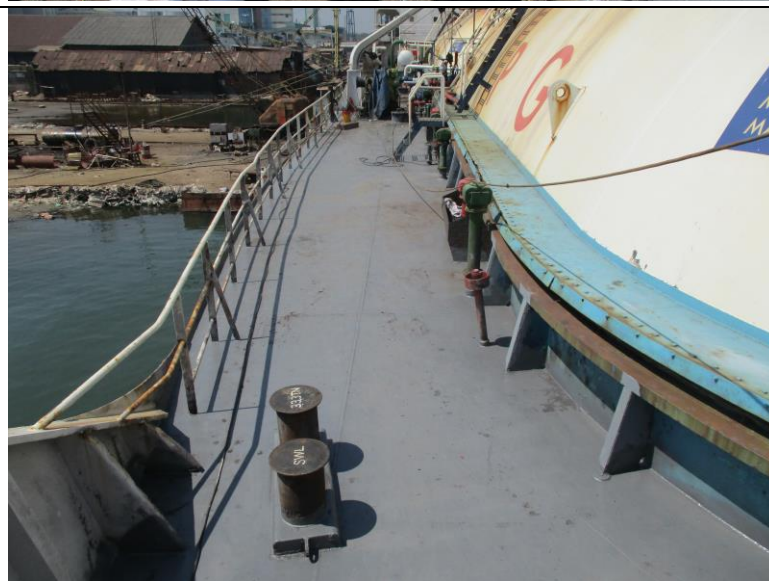

Main deck has been cleaned prior application finish coat blue



Pipe line for shower cargo dome has been renewed

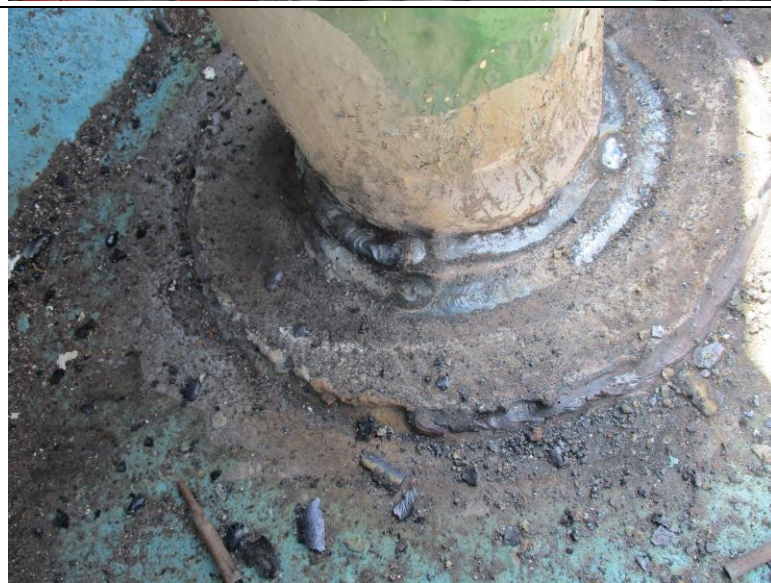

In progress repair welding doubling on forecastle deck for air vent pipe



Corroded air vent pipe has been renewed



In progress install new cargo piping
on cargo dome no 1



In progress install new cargo piping
on cargo dome no 1



In progress repair flexible joint
from pressure relief valve due to
holed



In progress chipping corroded pipe and valves on cargo dome by deck crew



In progress service and calibration OWS



Vinyl floor mess room has been renewed



In progress fabrication cargo piping
in work shop
